



Your trusted partner for buying, selling, and managing property,
ensuring hassle-free service with 100% transparency.

3/350/2 Mettukuppam,
OMR Thoraipakkam,
Chennai, India

hello@verified.realestate

+91 9996 12 9996

Official Property Record

Digitally Verified Record - Powered by Verified  RealEstate™



Project - Quarterly Progress Report (QPR)

Promoter's Name	:	M/s. Tamil Nadu Urban Habitat Development Board, Tiruppur Division, Tiruppur
Project Name	:	Construction of 832 Nos of Slum Tenements (G+3 Four Storied) at Anna Nagar, Mallagoundan palayam, Chithode Town Panchayat of Erode District under PMAY – HFA – AHP
Project Registration No.	:	TN/32/Building/0109/2020
Project Registration Date	:	06.03.2020
Project Completion Date	:	31.03.2025
Quarter Ending	:	September 2024

RERA Separate Bank A/c Details

Bank Name	:	IDBI Bank
Bank Branch	:	Avinashi Road
Bank A/c No.	:	1906104000074494

Amount collected from the allottees and deposited in the RERA A/c	:	
Amount withdrawn from the RERA A/c datewise with percentage of physical completion	:	
Bank statement for the respective Quarter duly signed by the Bank to be enclosed	:	

A. Sales

Sl. No.	Description	Cumulative No. of Units upto the Quarter	Total Area (Sq.m.)
1.	a) Flats Booked (As given in Carpet Area Statement while registration) Block / Tower Floor-wise	832	30958.72 Sq.m
	b) UDS Registered		

2. Furnish the details Flat-wise

Sl. No.	Flat No. as in approved Plan	Flats Booked (Yes/No)	UDS Registered (Yes/No)
1.	410 Beneficiaries paid the full beneficiary contribution and 131 beneficiaries paid the part beneficiary contribution and lott yet to be conducted		

B. Construction

Sl. No.	Description	Block/Tower No.	Status
1.	Stage of construction of each Block/Tower. Floor-wise	Block 1 to 26	Enclosed
2.	Status of Common Amenities for each Block/Tower, Item-wise as per approved plan		Enclosed
3.	Status of other Common Amenities as indicated in the Construction Agreement		Enclosed

Sl. No.	Description	Percentage
1.	Percentage of completion Block / Tower Floor-wise i) Physical ii) Financial (Enter Anticipated Project Cost in Lakhs)	92%
2.	Percentage of completion of Common Amenities i) Physical ii) Financial (Enter Anticipated Project Cost in Lakhs)	92%

C. Latest Colour Photo of all Blocks/Tower elevation including Common Amenities with Geotag and Date (Atleast from 2 angles)

Signed by Chartered Accountant



MMR
18/11/2023
AE

Q. Jayaraman
18/11/2023
Aem


Signed by Promoter

[Signature]
18/11/2023
Executive Engineer
TNUHQA / Tiruppur Division

STP Photos

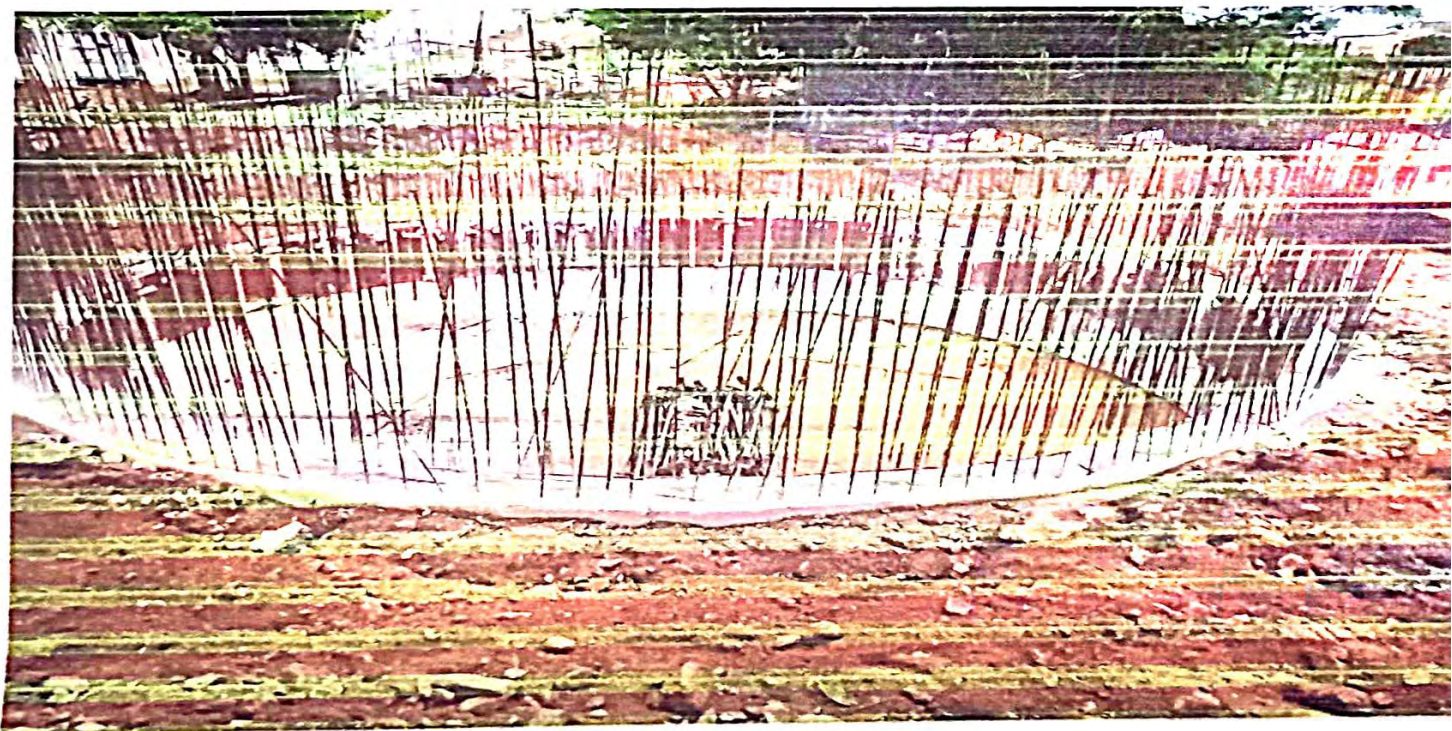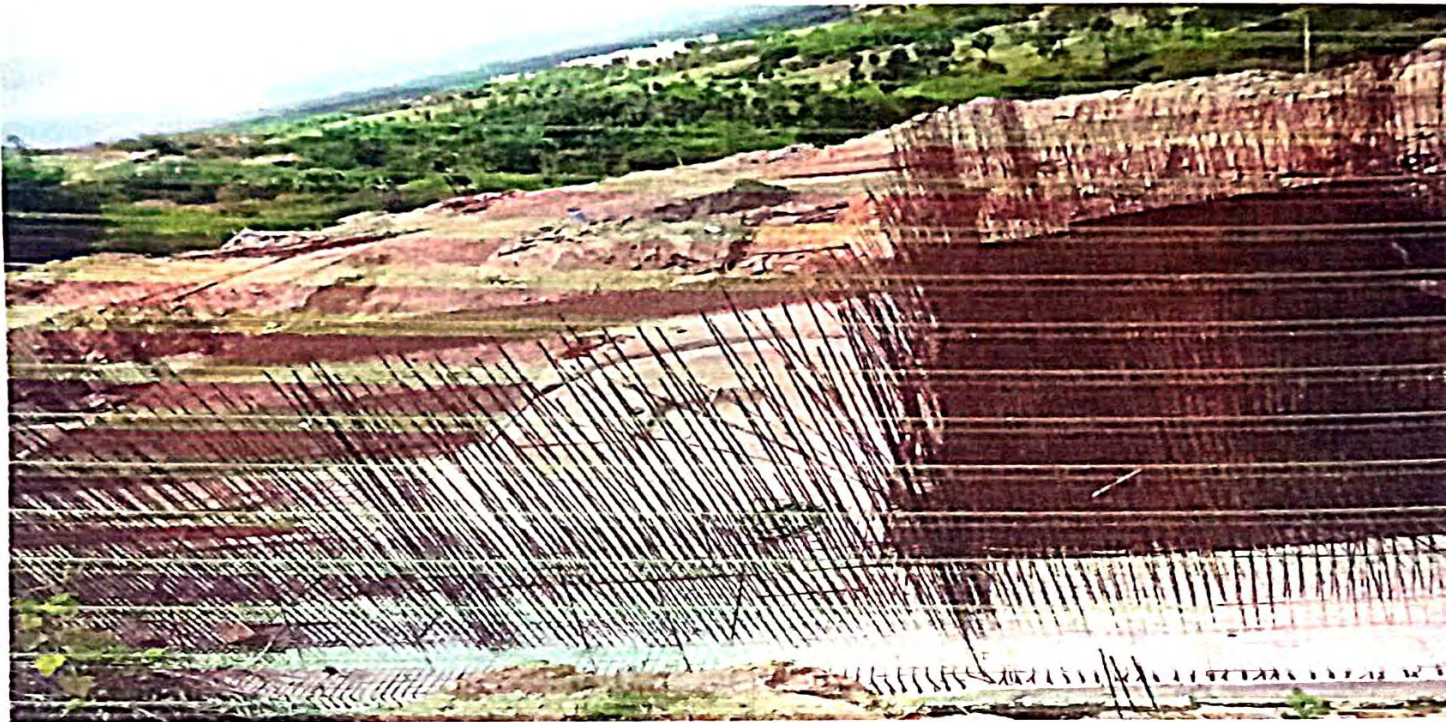


Water Supply Photos

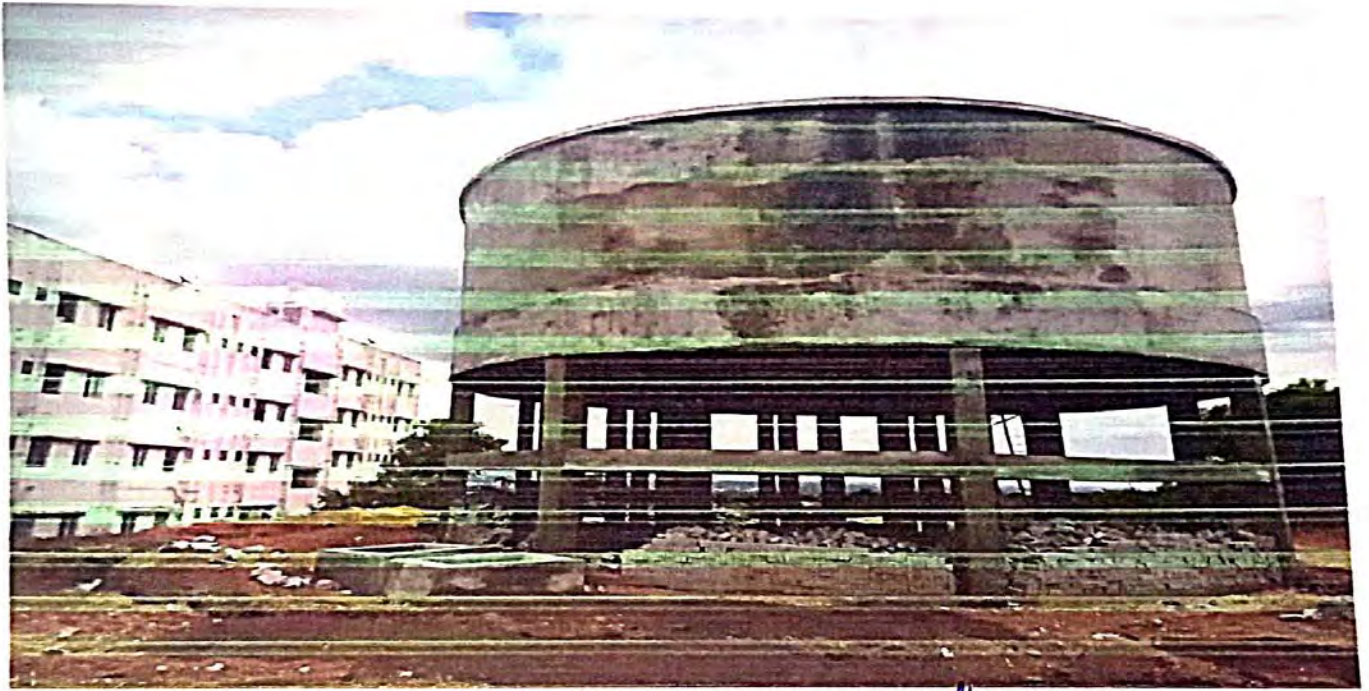


NMA
18/11/24
AE


Q. Jayaraj
18/11/24
AE


18/11/2024
Executive Engineer
TNUHDB / Tiruppur Division

[illegible]

Description	Block 14	Block 15	Block 16	Block 17	Block 18	Block 19	Block 20	Block 21	Block 22	Block 23	Block 24	Block 25	Block 26
Foundation	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
Ground Floor Slab	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
First Floor Slab	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
Second Floor Slab	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
Third Floor Slab	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
Internal Plumbing	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
Internal Flooring	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
UPVC Windows / Grills	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
Internal Putty	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
External Painting	31.12.2024												
UG Sump and Pump room	31.01.2025												
Electrical works	31.12.2024												
Sewer Line and STP	15.03.2025												
Road	28.02.2025												
Plinth Protection Wall	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed	Completed
Rain Water Harvesting	31.12.2024												


 M. M. A.
 10/1/24
 AE


 M. M. A.
 10/1/24
 TNUHDB / Trappur Division



our services doesn't just end there



Buying & Selling Services

Property Buying Assistance, Property Selling Support, Market Price Analysis, Owner Outreach and Negotiation.



Legal & Documentation Services

Certified EC, Patta, legal opinions, property verification, due diligence, litigation solutions, and legal heir certificates.



Property Development & Approvals

Building plan approvals, construction, layout and sub-division approvals, zone conversion, and occupancy certification.



NRI & Investment Services

Escrow Services, Rentals, Litigation Solutions, Property Valuation and Property Management



Compliance & Special Services

Demolition, Vaasthu checks, regularization of unauthorized buildings, and office space solutions.



 **empowering your real estate decisions**
with smart tools



Property Valuation & Cost Estimation

Guideline Value, Apartment Composite Value, Stamp Duty & Registration Fees Calculator, Building Value Calculator, Capital Gains Calculator, Area Unit Converter, Length Unit Converter



Ownership, Compliance & Legal Verification

Encumbrance Certificate (EC) Search, Find Your SRO, Temple Property Check, WAQF Property Check, View Patta/Chitta, View FMB, Patta Analyzer, EC Analyzer



Zoning & Land Use Analysis

Land Use Zone Finder, CRZ Zone Check, Aquifer Zone Check, CBA Check, EWS Check, Road Width Check, Proposed Road Widening Check, FSI Calculator



Property Documentation & Workflow Tools

Forms & Templates, Document Generator, Document Translation, Dictionary



Vastu & Property Management Tools

Home Vastu Shastra, Plot Vastu Shastra, Property Management



We're honored to be part of your
real estate journey

3/350/2 Mettukuppam,
OMR Thoraipakkam,
Chennai, India

hello@verified.realestate
[+91 9996 12 9996](tel:+919996129996)
www.verified.realestate
