



Your trusted partner for buying, selling, and managing property,
ensuring hassle-free service with 100% transparency.

3/350/2 Mettukuppam,
OMR Thoraipakkam,
Chennai, India

hello@verified.realestate

+91 9996 12 9996

Official Property Record

Digitally Verified Record - Powered by Verified  RealEstate™



Project - Quarterly Progress Report (QPR)

Promoter's Name	:	M/s.THE NEST
Project Name	:	NEST STELLAR
Project Registration No.	:	TN/35/Building/430/2023
Project Registration Date	:	17.10.2023
Project Completion Date	:	31.01.2025
Quarter Ending	:	DECEMBER - 2024

RERA Separate Bank A/c Details

Bank Name	:	ICICI BANK
Bank Branch	:	Nelson Manickam Road
Bank A/c No.	:	777705120040

Amount collected from the allottees and deposited in the RERA A/c from the date of opening	:	Rs.6,78,93,818/-
Amount withdrawn from the RERA A/c from the date of opening	:	Rs.4,75,00,000/-
Bank statement for the last one year duly signed by the Bank to be enclosed	:	Enclosed

A. Sales

Sl. No.	Description	Cumulative No. of Units upto the Quarter	Total Area (Sq.m.)
1.	a) Flats Booked (As given in Carpet Area Statement while registration) Block / Tower Floor-wise	15	1789.30
	b) UDS Registered	15	789.67

2. Furnish the details Flat-wise

Sl. No.	Flat No. as in approved Plan	Flats Booked (Yes/No)	UDS Registered (Yes/No)
1.	A1	YES	YES
2.	A2	YES	YES
3.	A3	YES	YES
4.	A4	YES	YES
5.	A5	YES	YES
6.	B1	YES	YES
7.	B2	YES	YES
8.	B3	YES	YES
9.	B4	YES	YES
10.	B5	YES	YES
11.	C1	YES	YES
12.	C2	YES	YES
13.	C3	YES	YES
14.	C4	YES	YES
15.	C5	YES	YES

B. Construction

Sl. No.	Description	Block/Tower No.	Floor-wise Status
1.	Stage of construction of each Block/Tower, Floor-wise	1	Completed
2.	Status of Common Amenities for each Block/Tower, Item-wise as per approved plan	NIL	NIL
3.	Status of other Common Amenities as indicated in the Construction Agreement	NIL	NIL

Sl. No.	Description	Percentage
1.	Percentage of completion Block / Tower Floor-wise	
	i) Physical	100%
	ii) Financial (Enter Anticipated Project Cost in Lakhs)	Rs. 6,11,04,436/-
2.	Percentage of completion of Common Amenities	
	i) Physical	NIL
	ii) Financial (Enter Anticipated Project Cost in Lakhs)	NIL

C. Latest Colour Photo of all Blocks/Tower elevation including Common Amenities with Geotag and Date (Atleast from 2 angles) – Enclosed

K. Karthik



Signed by Chartered Accountant


For THE NEST
[Signature]
Managing Partner

Signed by Promoter


SITE PHOTOS (Outer view)



SITE PHOTOS (Inner view)

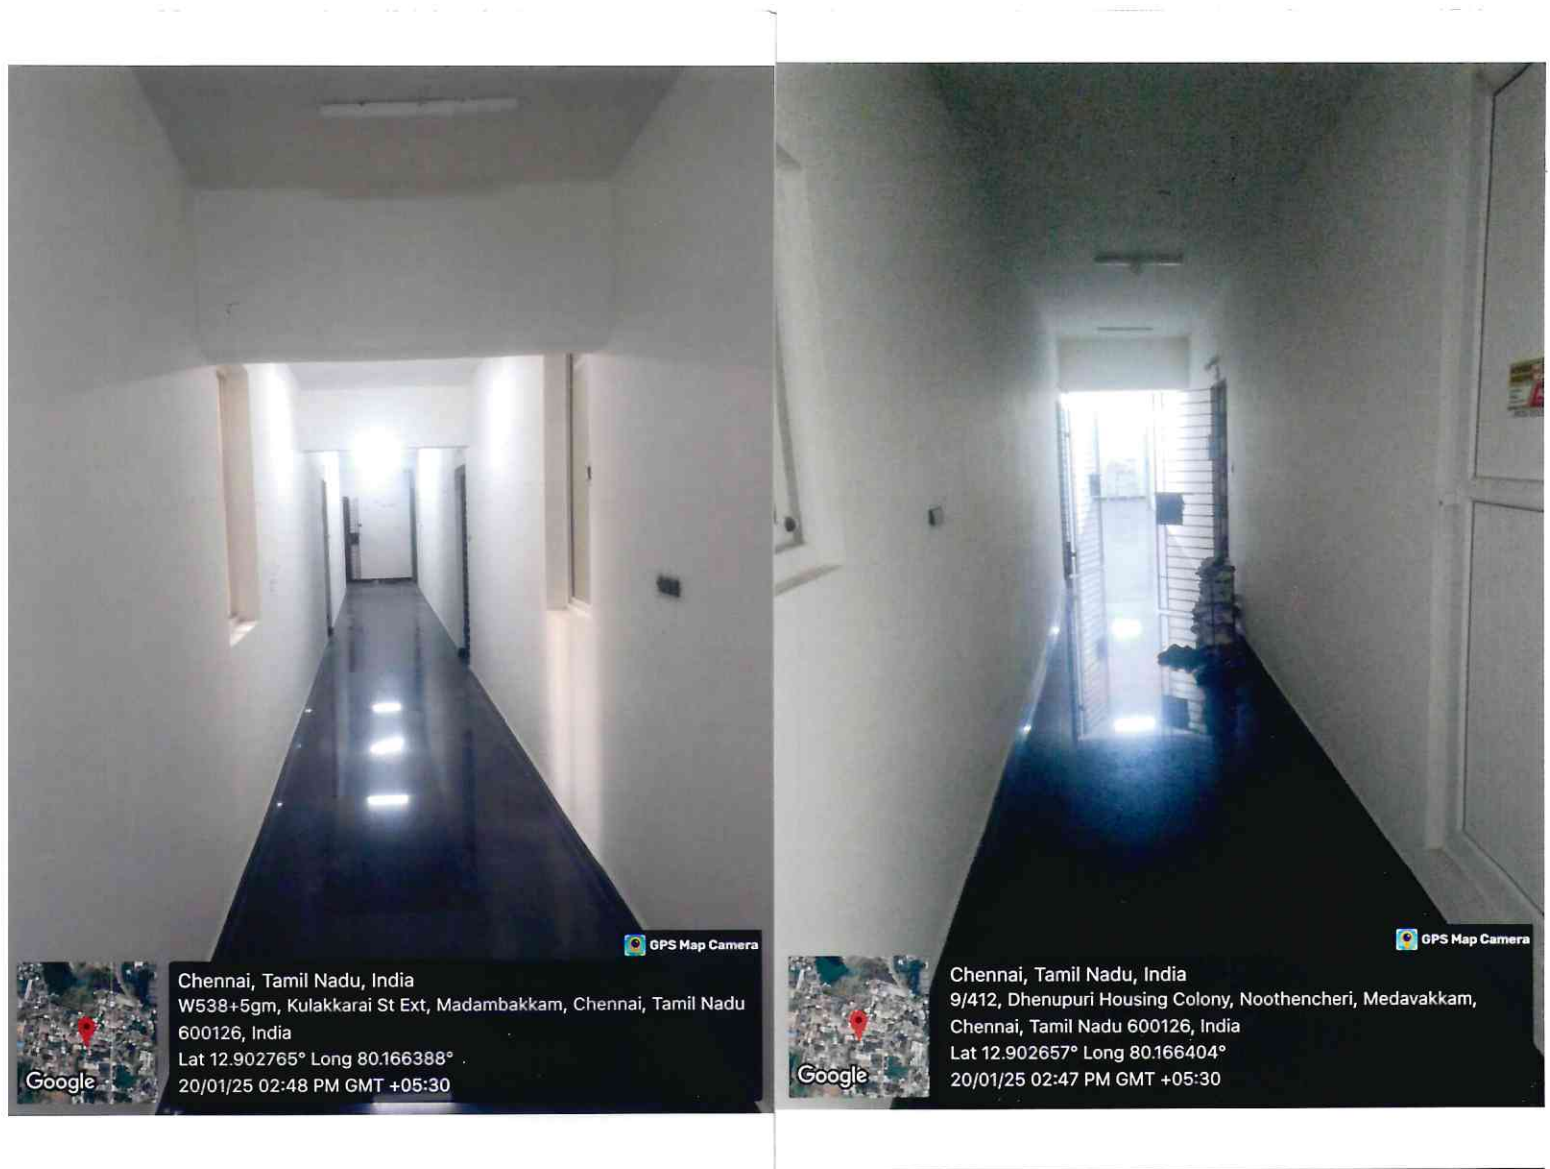

AMENITIES

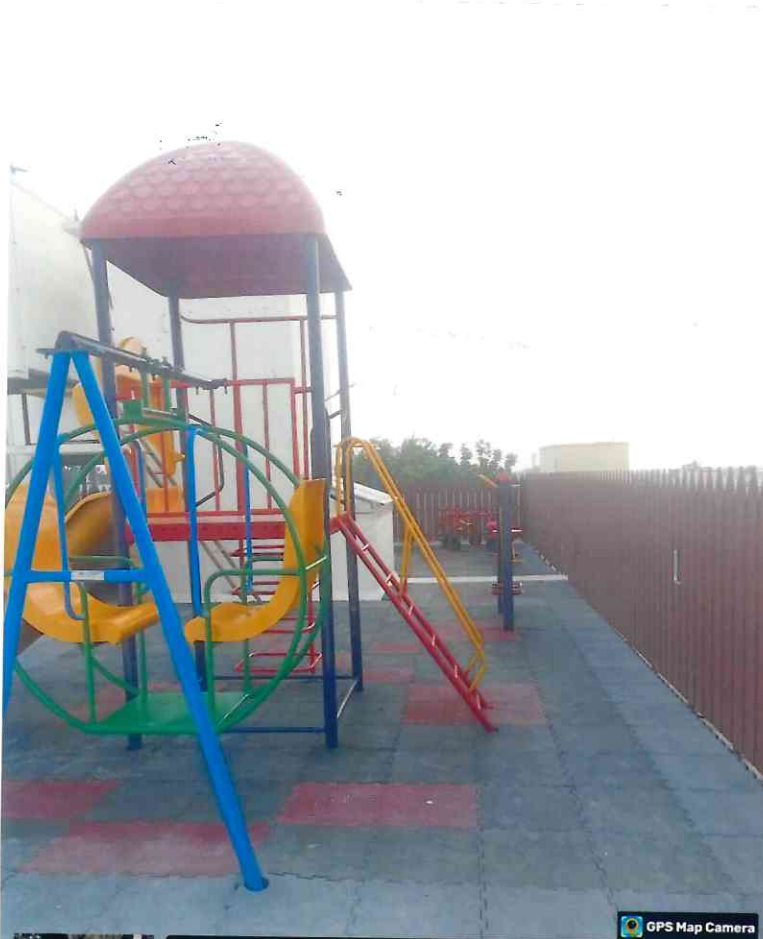

Chennai, Tamil Nadu, India
W538+5gm, Kulakkarai St Ext, Madambakkam, Chennai, Tamil Nadu
600126, India
Lat 12.902802° Long 80.166337°
20/01/25 02:43 PM GMT +05:30


GPS Map Camera



Chennai, Tamil Nadu, India
W538+4f7, Kulakkarai St Ext, Madambakkam, Chennai, Tamil Nadu
600126, India
Lat 12.902682° Long 80.166318°
20/01/25 02:45 PM GMT +05:30

GPS Map Camera

AMENITIES

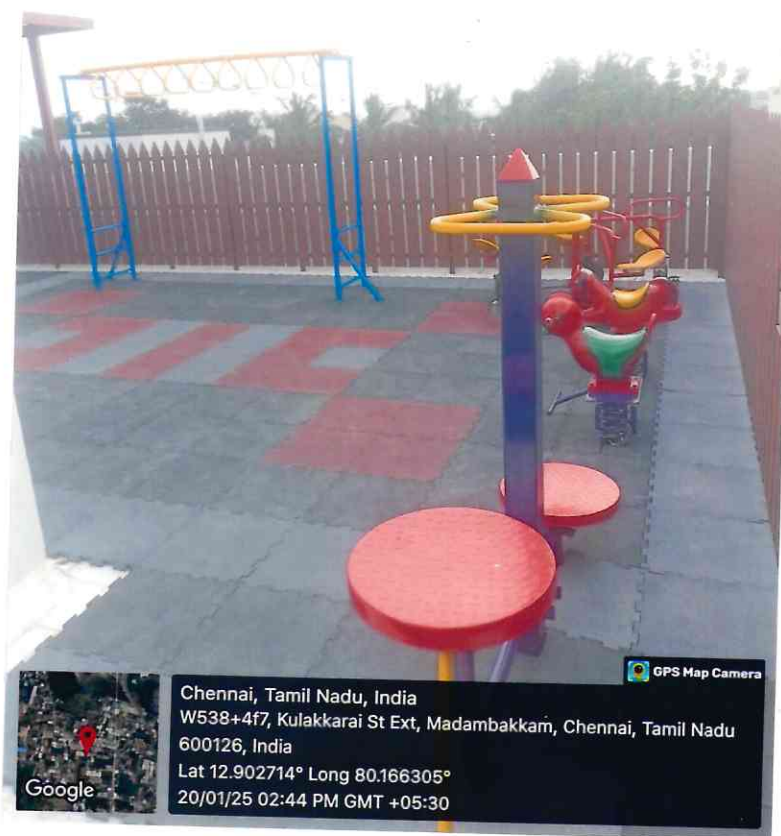



CHENNAI METROPOLITAN DEVELOPMENT AUTHORITY

Thalamuthu Natarajan Building
No. 1, Gandhi Irwin Road, Egmore, Chennai - 600 008.



கலைஞர்
100
BY RPAD
1924 - 2023

COMPLETION CERTIFICATE

From

The Member-Secretary
Chennai Metropolitan
Development Authority
"Thalamuthu-Natarajan Building"
No.1, Gandhi-Irwin Road,
Egmore, Chennai-600 008

To

- 1) The Chairman, TANGEDCO,
Anna Salai, Chennai-600 002.
- 2) The Commissioner,
St.Thomas Mount Panchayat Union,
Chitlapakkam, Chennai-600 064.

Letter No.CMDA/CC/NHRB/S/0269/2024

Dated:04.10.2024

Sir / Madam,

Sub: CMDA – Enforcement Cell (South-II) – Completed Construction of a Stilt Floor + 3 Floors Residential Building with 15 Dwelling Units at Plot No.1 (As per CMDA approved subdivision No.P.P.D/L.O No.155/2023) Indira Nagar, Kulakarai Street Extension, Vengaivasal, Chennai comprised in S.No.252/1A1C (Part) of Vengaivasal Village within the Limits of the St.Thomas Mount Panchayat Union – Applied for Completion Certificate – Completion Certificate – Issued – Reg.

- Ref: 1. W.P(MD) No.8948 of 2019 & W.M.P.(MD) Nos.6912 & 6913/2019 dated 12.04.2019.
2. CMDA Planning Permission No.OL-PP/NHRB/0310/2023, in Planning Permit No.OL-00451 in letter No. CMDA/PP/NHRB/S/0452/2023 dated 12.08.2023.
3. Online Completion Certificate Application received from M/s.The Nest, Represented by its Managing Partner Thiru.M.Shanker Ganesh dated 03.07.2024.
4. This office D.C.Letter even No. dated 24.09.2024.
5. The applicant has remitted Additional Development Charges & Infrastructure and Amenities Charges vide CMDA Receipt No.B0026146 dated 25.09.2024 with enclosures.

This is to certify that M/s.The Nest, Represented by its Managing Partner Thiru.M.Shanker Ganesh, has completed the Construction of a Stilt Floor + 3 Floors Residential Building with 15 Dwelling Units at Plot No.1 (As per CMDA approved subdivision No.P.P.D/L.O No.155/2023) Indira Nagar, Kulakarai Street Extension, Vengaivasal, Chennai comprised in S.No.252/1A1C (Part) of Vengaivasal Village within the Limits of the St.Thomas Mount Panchayat Union for which Planning Permission was accorded in the reference 2nd cited. It was inspected and observed that the building has been completed as per the approved plan and satisfies the Norms for the issue of a Completion Certificate prescribed in Annexure XXIII of TNCDBR, 2019.

Contd.,

CMDA/CC/NHRB/S/0269/2024

2. Accordingly Completion Certificate is issued for the above construction in C.C.No.EC/South-II/ 340 / 2024, dated 04.10.2024.

3. In accordance with the provisions of the Town & Country Planning Act, 1971 and the Rules made there under. This Provision does not cover the Structural Stability aspect of the building. As far as the Structural Stability aspect of the building is concerned, it falls within the jurisdiction of the Local Body concerned as stated in the connected Building Rules under the respective Local Body Act, 1920, such as Madras City Municipal Corporation Act, 1919, Tamil Nadu District Municipality Act, Tamil Nadu Panchayat Act. The Completion Certificate issued under rule 20 (6) Annexure XXIII of TNCDBR, 2019 does not cover the Structural Stability aspect. It is the sole responsibility of the Applicant/Developer/ Power Agent and the Structural Engineers/ Licensed Surveyor/Architects, who have signed in the Plan to ensure the safety after construction and also for the continued Structural Stability of the buildings.

4. Further, the Completion Certificate issued is subject to the outcome of the Hon'ble High Court order in the reference 1st cited (Also indicated in the Planning Permission approval letter in Serial No.11).

Yours faithfully,



for MEMBER-SECRETARY
04/10/24

Copy to:

1. M/s.The Nest, Represented by its
Managing Partner Thiru.M.Shanker Ganesh,
New No.15, Old No.60, Kamaraj Nagar 4th Street,
Choolaimedu,
Chennai – 600 094.
2. The Chairperson,
TNRERA,
CMDA Tower-II, 1st Floor, Egmore,
Chennai – 600 008.
(TNRERA Project Registration Certificate
No.TN/35/Building/430/2023, dated
17.10.2023 with the project name of “NEST
STELLAR” in file No.TNRERA/08837/
2023 with the valid period till January 2025
in the name of The Nest Represented by its
Managing Partner Thiru.M.Shanker
Ganesh).
3. The Deputy Financial Analyst
Finance Division, CMDA.
(For Refund of Security Deposit for
Building, Display Board and Septic Tank)
4. The System Analyst, Computer Cell, CMDA For Web-hosting
(to update Webpage).

Note:

- (i) The original copy of CMDA's Cash Receipt No.CMDA/PP/Ch/11586/2023, dated 07.08.2023 for the payment of the Security Deposit has been submitted by the applicants.
- (ii) If any change in the name of the Security Deposit payee an Indemnity Bond in the prescribed format along with NOC from the applicant is to be furnished.

FORM-4A
ARCHITECT'S CERTIFICATE
(To be furnished on completion of building)

To

Date: 06.02.2025

M/s. THE NEST,
Rep.by its Managing Partner Mr.M.Shanker Ganesh,
New No.15, Old No.6,
Kamarajar Nagar 4th Street,
Choolaimedu, Chennai – 600 094.,

Subject: Certificate of Completion of Construction Work of NEST STELLAR Building, 1 Block of the Building of the Project (TNRERA Registration Number. TN/35/Building/430/2023, dated 17.10.2023) situated on the Land Plot No.1, bearing S.No.252/1A1C (Part), demarcated by its boundaries (latitude and longitude of the end Points) to the North to the South 12.902858" to the East to the West 80.166342" of Indira Nagar, Kulakkarai Street Extension, Vengaivasal Village, Tambaram Taluk, Chengalpet District measuring 789.67 sq.mts. area being developed by M/s. THE NEST.

Sir,

I Mrs.M.SATHYA have undertaken the assignment as Architect/Engineer for certifying the completion of Construction Work of NEST STELLAR Building, 1 Block of the Building situated on the Plot No.1, Comprised in S.No.252/1A1C (Part), Indira Nagar, Kulakkarai Street Extension, Vengaivasal Village, Tambaram Taluk, Chengalpet District measuring 789.67 sq.mts. area, being Developed by M/s. THE NEST.

2. Following technical professionals have been appointed by Owner/promoter: (as applicable)

- (i) Tmt.P.ELANKANI as Architect
- (ii) Thiru.B.SRINIVASAN as Structural Consultant
- (iii) Thiru.KARTHI.V as MEP Consultant
- (iv) Thiru.N.VELMANI as Site Supervisor

3. Based on the detailed inspection of the building and structural safety certificate issued by the Structural Engineer and to the best of my knowledge, I hereby certify that NEST STELLAR Building, 1 Block of the Building has been completed in all aspects as per the planning permission issued by the competent authority and building permission issued by the local body concerned. The NEST STELLAR Building, 1 Block of the Building is granted Completion Certificate bearing number CMDA/CC/NHRB/S/0269/2024, dated 04.10.2024 by Chennai Metropolitan Development Authority.

Yours Faithfully,

M. SATHYA (M. SATHYA)

Signature & Name (IN BLOCK LETTERS) of Architect with (CA No. CA/2013/60713.)

FORM-4B

**STRUCTURAL STABILITY CERTIFICATE BY
REGISTERED STRUCTURAL ENGINEER**
(To be furnished on completion of building)

I, B.SRINIVASAN have undertaken assignment as Structural Engineer for the detailed design and construction of the building NEST STELLAR, 1 Block of the building comprising of Three Floors situated in Plot No.1, bearing Survey Number.252/1A1C (Part) Indira Nagar, Kulakarai Street Extension, Vengaivasal Village, Tambaram Taluk, Chengalpet District, PIN - 600 126.


It is certified that the building has been designed as a RCC structure to withstand the dead load, imposed load and wind load/earthquake loads ensuring structural safety and serviceability as per the norms and guidelines prescribed in applicable relevant standards and Codes of Bureau of Indian Standards.

Further after the detailed inspection of the building, it is certified that the constructed building is structurally safe and sound for the purpose for which it is constructed.

Yours faithfully,


B.SRINIVASAN, B.E., A.M.I.E., C.Engg.
Structural Engineer Grade - II
CMDA Reg No. S.E/GR-II/19/08/152
176/311, ARCOT ROAD,
KODAMBAKKAM, CHENNAI-600 024

Signature, Name and seal of
the Registered Structural Engineer



our services doesn't just end there



Buying & Selling Services

Property Buying Assistance, Property Selling Support, Market Price Analysis, Owner Outreach and Negotiation.



Legal & Documentation Services

Certified EC, Patta, legal opinions, property verification, due diligence, litigation solutions, and legal heir certificates.



Property Development & Approvals

Building plan approvals, construction, layout and sub-division approvals, zone conversion, and occupancy certification.




NRI & Investment Services

Escrow Services, Rentals, Litigation Solutions, Property Valuation and Property Management



Compliance & Special Services

Demolition, Vaasthu checks, regularization of unauthorized buildings, and office space solutions.



 **empowering your real estate decisions**
with smart tools



Property Valuation & Cost Estimation

Guideline Value, Apartment Composite Value, Stamp Duty & Registration Fees Calculator, Building Value Calculator, Capital Gains Calculator, Area Unit Converter, Length Unit Converter



Ownership, Compliance & Legal Verification

Encumbrance Certificate (EC) Search, Find Your SRO, Temple Property Check, WAQF Property Check, View Patta/Chitta, View FMB, Patta Analyzer, EC Analyzer



Zoning & Land Use Analysis

Land Use Zone Finder, CRZ Zone Check, Aquifer Zone Check, CBA Check, EWS Check, Road Width Check, Proposed Road Widening Check, FSI Calculator



Property Documentation & Workflow Tools

Forms & Templates, Document Generator, Document Translation, Dictionary



Vastu & Property Management Tools

Home Vastu Shastra, Plot Vastu Shastra, Property Management



We're honored to be part of your
real estate journey

3/350/2 Mettukuppam,
OMR Thoraipakkam,
Chennai, India

hello@verified.realestate
[+91 9996 12 9996](tel:+919996129996)
www.verified.realestate
